

Project Information								
Surveyor Name	BUENO_R Certificate Number		P0043820-082023					
Owner		Customer	RIVERBEND OF NAPLES MOBILE HOA					
Drainage Area		PO Number	231753					
Pipe Segment	MH-1 - MH-4	Date	11/30/2023 18:33					
Reference Street	WALKERBILT RD	City	NAPLES					
Comments		ony						
Manhole								
Upstream MH	1	Rim to Invert (U)						
Grade to Invert (U)		Rim to Grade (U)						
Downstream MH	4	Rim to Invert (D)						
Grade to Invert (D)		Rim to Grade (D)						
Sewer Use	Sanitary	Direction of Survey	Downstream					
	F	Pipe						
Height (Diameter)	6	Width						
Shape	Circular	Material	Polyvinyl Chloride					
Lining Method		Pipe Joint Length						
Total Length		Length Surveyed	26.1					
Year Laid		Year Renewed						
		lisc						
Flow Control	Not Controlled	Media Label	DVD					
Purpose	Routine Assessment	Sewer Category	11/20/2022 10 24					
Pre-Cleaning	Jetting	Date Cleaned	11/30/2023 18:34					
Weather	Dry	Location Code	Main Highway - Suburban/Rural					
Additional Info		Location Details						
	Cu	stom						
Number of Taps		Number of Roots						
Num Cracks /		Number of Broken /						
Fractures		Holes / Collapse						
Number of Deposits Custom7		Custom6 Struct Grade						
OM Grade		Overall Grade						
	Da							
	ra ra	ICP 6 Sheet (Group)						
Reverse Setup ID		Number						
Imperial Units (US)	True	Pressure Value						
Work Order		Project	RIVERBEND OF NAPLES SANITARY 11.30.2023					
		Completed	No					
Created with the TOSM report generator								

Project: RIVERBEND OF NAPLES SANITARY 11.30.2023

Date: 11/30/2023 6:33:00 PM Street: WALKERBILT RD Length Surveyed: 0 Pacp Quick Overall Rating: 2200 Height (Diameter): 6 Street: WALKERBILT RD Pipe Segment Reference: MH-1 - MH-4 Upstream MH: 1 Downstream MH: 4 Direction of Survey: Downstream Material: Polyvinyl Chloride

Distance	Fault Observation	Time	Picture
0.0	Manhole Severity: None Remarks: 1	01:01	MH 1 TO MH 4 RIVERBEND OF NAPLES SANITARY 11.30.2023
0.0	Water Level Severity: None Percent: 5	01:36	MH 1 TO MH 4 RIVERBEND OF NAPLES SANITARY 11.30.2023
6.1	Tap Factory Position: 12 Severity: None Size: 6	02:36	MH 1 TO MH 4 RIVERBEND OF MAPLES SANITARY 11.30.2023 Table Factory 11.30.2023 6.12 ft

Distance	Fault Observation	Time	Picture
22.7	Material Change Severity: None Remarks: VCP	04:13	MH 1 TO MH 4 RIVERBEND OF NAPLES SANITARY 11.30.2023
25.9	Joint Offset Large Severity: None Remarks: INFIL DRIPPER Struct Weight: 2	05:29	MH 1 TO MH 4 RIVERBEND OF NAPLES SANITARY 11.30.2023 Joint Offset Large 11.30.2023 25.88 ft 644 mbar 790 mbar
26.0	Abandoned Survey Severity: None Remarks: CANT MAKE IT PASS JOINT	07:39	MH 1 T0 MH 4 RIVERBEND OF NAPLES SANITARY 11.30.2023


Distance	Fault Observation	Time	Picture
26.1	Joint Separated Large Severity: None Struct Weight: 2	06:05	MH 1 TO MH 4 RIVERBEND OF NAPLES SANITARY 11.30.2023 Doint Separated Large 11.30.2023 26.12 ft

Project: RIVERBEND OF NAPLES SANITARY 11.30.2023

Date: 11/30/2023 6:33:00 PM Street: WALKERBILT RD Length Surveyed: 0 Pacp Quick Overall Rating: 2200 Height (Diameter): 6 Street: WALKERBILT RD

Pipe Segment Reference: MH-1 - MH-4 Upstream MH: 1 Downstream MH: 4 Direction of Survey: Downstream Material: Polyvinyl Chloride



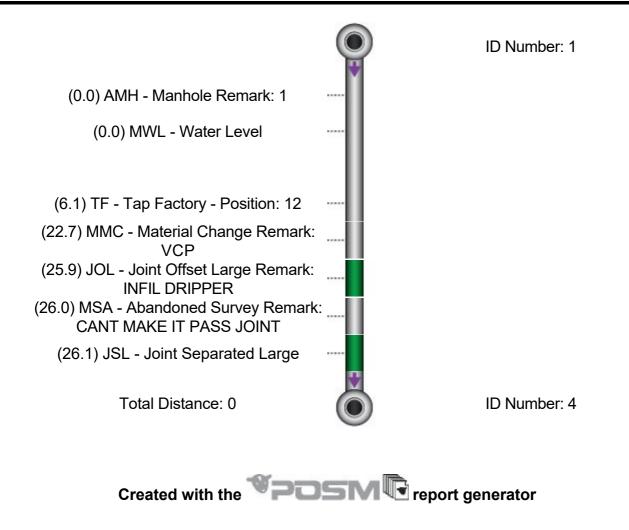

Nassco C.C.T.V. Defect Code Information

Grade	Structural	O&M	Overall
5	0	0	0
4	0	0	0
3	0	0	0
2	4	0	4
1	0	0	0
Overall	4	0	4
Number of Defects	2	0	2
Pipe Rating	2200	0000	2200
Pipe Ratings Index	2	0	2

Nassco C.C.T.V. Defect Code Information

Distance Video Ref	Video	C . L	Cont	Value			Laint	Circumferential Location	
	Code	Defect	Dimension		% J	Joint	At /	То	
				1st	2nd	70		From	10
0	61	AMH - Manhole							
		1							
0	96	MWL - Water Level				5			
6.1	156	TF - Tap Factory		6				12	
22.7	253	MMC - Material Change							
		VCP							
25.9	329	JOL - Joint Offset Large							
	INFIL DRIPPER								
26	459	MSA - Abandoned Survey							
	CANT MAKE IT PASS JOINT								
26.1	365	JSL - Joint Separated Large							

Videos Created for Session RIVERBEND OF NAPLES SANITARY 11.30.2023


1-4_11302023-1834-D.mp4 Size: 186 MB

Your browser does not support the video tag.

Project: RIVERBEND OF NAPLES SANITARY 11.30.2023

Date: 11/30/2023 6:33:00 PM Street: WALKERBILT RD Length Surveyed: 0 Pacp Quick Overall Rating: 2200 Height (Diameter): 6 Street: WALKERBILT RD Pipe Segment Reference: MH-1 - MH-4 Upstream MH: 1 Downstream MH: 4 Direction of Survey: Downstream Material: Polyvinyl Chloride

Percent Grade Mean: -6.15 Plot Distance From: 0 To 1 Max Percent Difference: 3 Number of Window Values: 1 Percent Differnce Max for Windows Values: 60 Number of Feet to Average: 1 Final number of points plotted: 21

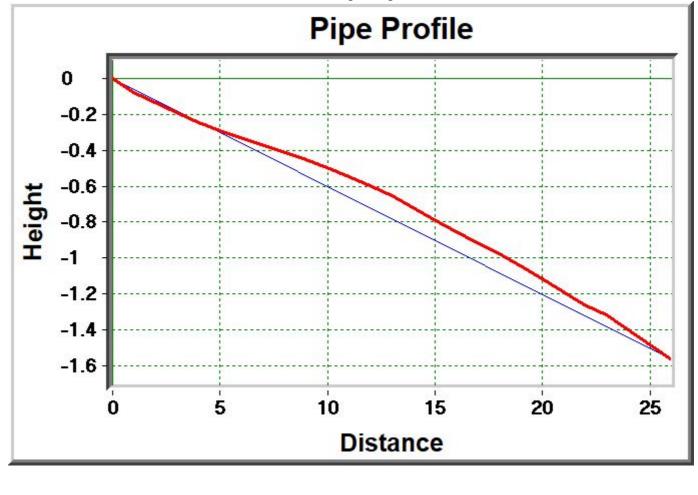

Additional Reports for Session RIVERBEND OF NAPLES SANITARY 11.30.2023
